

Monthly update

Hunter Street (Sydney CBD)

August 2024

John Holland CPB Contractors Ghella Joint Venture (JCG) has been awarded the contract to deliver 3.5 kilometres of twin metro rail tunnels between The Bays and Hunter Street and excavate the Pyrmont and Hunter Street metro stations.

Structural demolition at both our Hunter Street East and West sites is nearing completion, as we continue with demolition of the lower levels and building basements.

Below ground excavation is continuing in both the station cavern and turnback tunnels, with the team having almost completed excavation of the third heading inside the station cavern.

Preparations for upcoming shaft excavation are ongoing, and we continue with the installation of ground anchors and support works.

What work we're doing in August

- Excavation of the Hunter Street Station cavern and turnback tunnels using a roadheader and rock hammer
- Delivery and removal of materials, plant and equipment to Hunter Street East and West
- Structural demolition using an excavator with hammer or pulveriser
- Removal of scaffold and site hoarding
- Temporary storing of plant and equipment along site perimeters

- Temporary road, lane, and footpath closures to accommodate works around both sites and along tunnel alignment
- Ground and building support activities including support walls and rock anchoring.
- Use of tower and support cranes
- Utility identification, relocations, and disconnections
- Operation of concrete trucks and support vehicles
- Geotechnical investigations, including borehole drilling
- Removal of tower cranes at Hunter Street East and West
- Low impact site surveys and monitoring

When and where we'll be working

We'll be working at our Hunter Street East and West sites, and across the CBD.

Above ground standard working hours are between **7am to 6pm, Monday to Friday and 8am to 6pm, Saturday.**

We will be carrying out low-impact activities between **5am to 7am and 6pm to 8pm from Monday to Friday.** No noisy work will happen during these hours.

Underground tunnelling activities are undertaken 24 hours per day, seven days a week.

Above ground out-of-hours lookahead

Some above ground work is required outside standard construction hours to minimise impacts on traffic and to ensure the safety of pedestrians, motorists and workers. If required, out-of-hours work will occur in the CBD between **6pm and 7am Monday to Saturday**.

Noisy activities are scheduled to happen earlier in the night, and we aim to be completed by **12am**.

Below is a schedule of the out-of-hours at Hunter Street work over the next three months.

Activity	Aug	Sep	Oct
Low impact site surveys and monitoring	● ●	● ●	● ●
Utilities investigations and relocations	● ●	● ●	● ●
Delivery and removal of materials, plant and equipment to Hunter Street East and West	● ●	● ●	● ●
Removal of tower crane at Hunter Street East and West	● ●	● ●	
Temporary road, lane, and footpath closures	● ●	● ●	● ●
Ground and building support activities	● ●	● ●	● ●
Operation of concrete trucks and support vehicles	● ●	● ●	● ●
Hunter Street East ● Hunter Street West ●			

Managing our impacts

We aim to manage our work to avoid impacts to the community and the environment. Both our Hunter Street sites are designed to minimise impact.

This includes:

- Site planning and layout to reduce impacts
- Using quieter and less noise and vibration emitting construction methods where feasible and reasonable such as pulveriser attachments
- Installation of noise blankets where demolition is taking place.
- Dust suppression measures such as water mister attachments, water cannons, wheel washing and scaffold mesh.
- Adhering to agreed respite breaks.

Equipment used


Equipment used for underground work includes but is not limited to roadheaders, rockbolt rigs, shotcrete rigs, excavators with rock breaker, concrete trucks, dump trucks, cranes, light vehicles and traffic control vehicles.

Equipment used for above ground work includes but is not limited to drill rigs, concrete trucks, excavators with rock hammer and pulveriser attachments, saw cutters, specialised ground penetrating equipment, tower and support cranes, vacuum trucks, elevated work platforms, fork lifts, hand tools including jack hammers, roadsaws and rattle guns, water cannons, temporary fencing, lighting towers, excavators, trucks, light vehicles, traffic control equipment and generators.

Weekly email updates

Weekly email updates provide the latest information about upcoming work including roadheader excavation progress. If you'd like to receive these email updates, please send a request to MetroTunnelsJCGJV@transport.nsw.gov.au and we will add you to the distribution list.


Expected cavern excavation

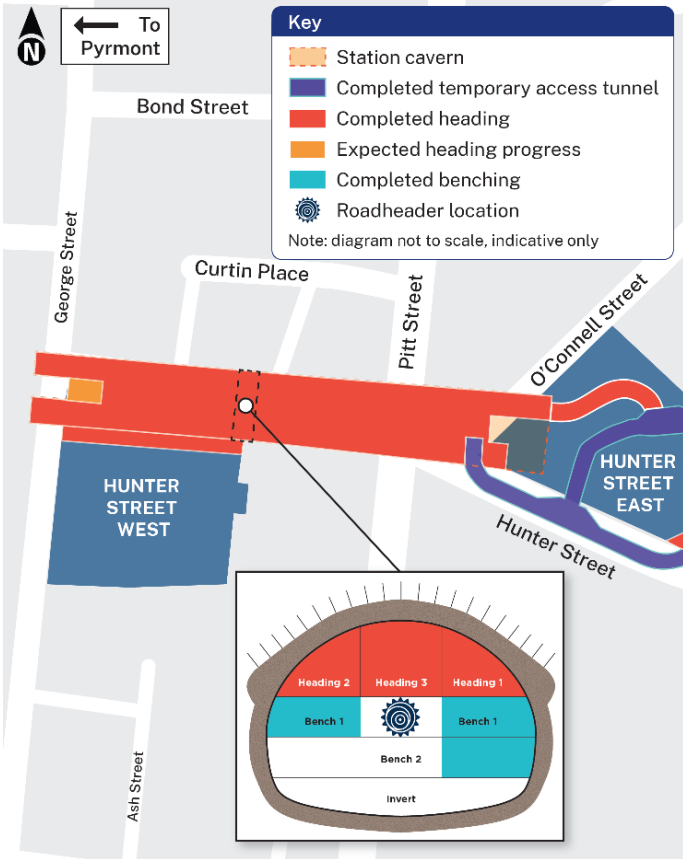

Expected turnback excavation



Above ground work locations

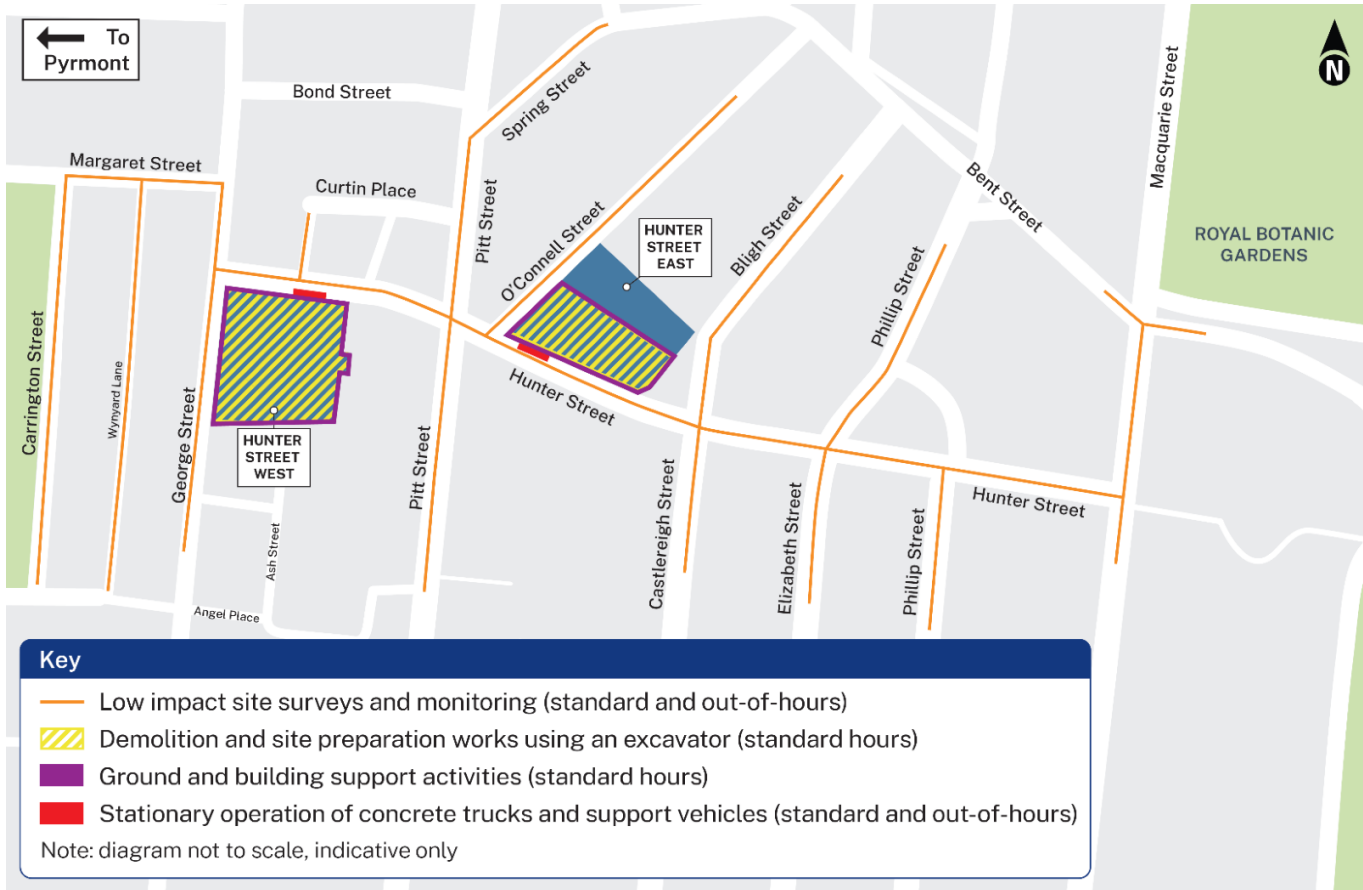

Contact us



24-hour Community Information Line **1800 612 173**



MetroTunnelsJCGJV@transport.nsw.gov.au



Sydney Metro West, PO Box K659,
Haymarket NSW 1240



Access information in over 100 languages Download
Sydney Metro Connect from the
App store or get it on Google Play.



Translating and interpreting service

If you need help understanding this information, please contact the Translating and Interpreting Service on **131 450** and ask them to call us on **1800 612 173**
